

HOWARD CHEVROLET

August 26, 1963

Mr. Marvin Howard, President
Howard's Chevrolet Company, Inc.
515 South Walnut Street
Bloomington, Indiana

Dear Mr. Howard:

Enclosed is the latest Plot Plan of your site. I believe the locations to be correct.

I want you to note the difference in grades between Mr. Stapleton and Mr. Strain's topo. I called Mr. Stapleton this morning, Monday, August 26, and found out he assumed an elevation of 500 from, I believe, a fire hydrant. He mentioned that Mr. Strain took his topo from a government topo print. These prints generally vary both horizontally and vertically.

I would like to suggest we have Mr. Stapleton take this Plot Plan and tie down these elevations. At the same time, I would like to have center line grades every 100' in front of the property. I will also show the general location of the septic system leaching field and if satisfactory with you, Mr. Stapleton should make a percolation test for the Health Department.

Thanking you for your continued cooperation.

Cordially,

PACKAGED BUILDINGS, INC.


W. M. Loxley, P.E.
W. M. Loxley, P.E.

WML: plp

encls.

cc. Mr. J. J. Dues
Mr. John Stapleton

*File Under
Howard*

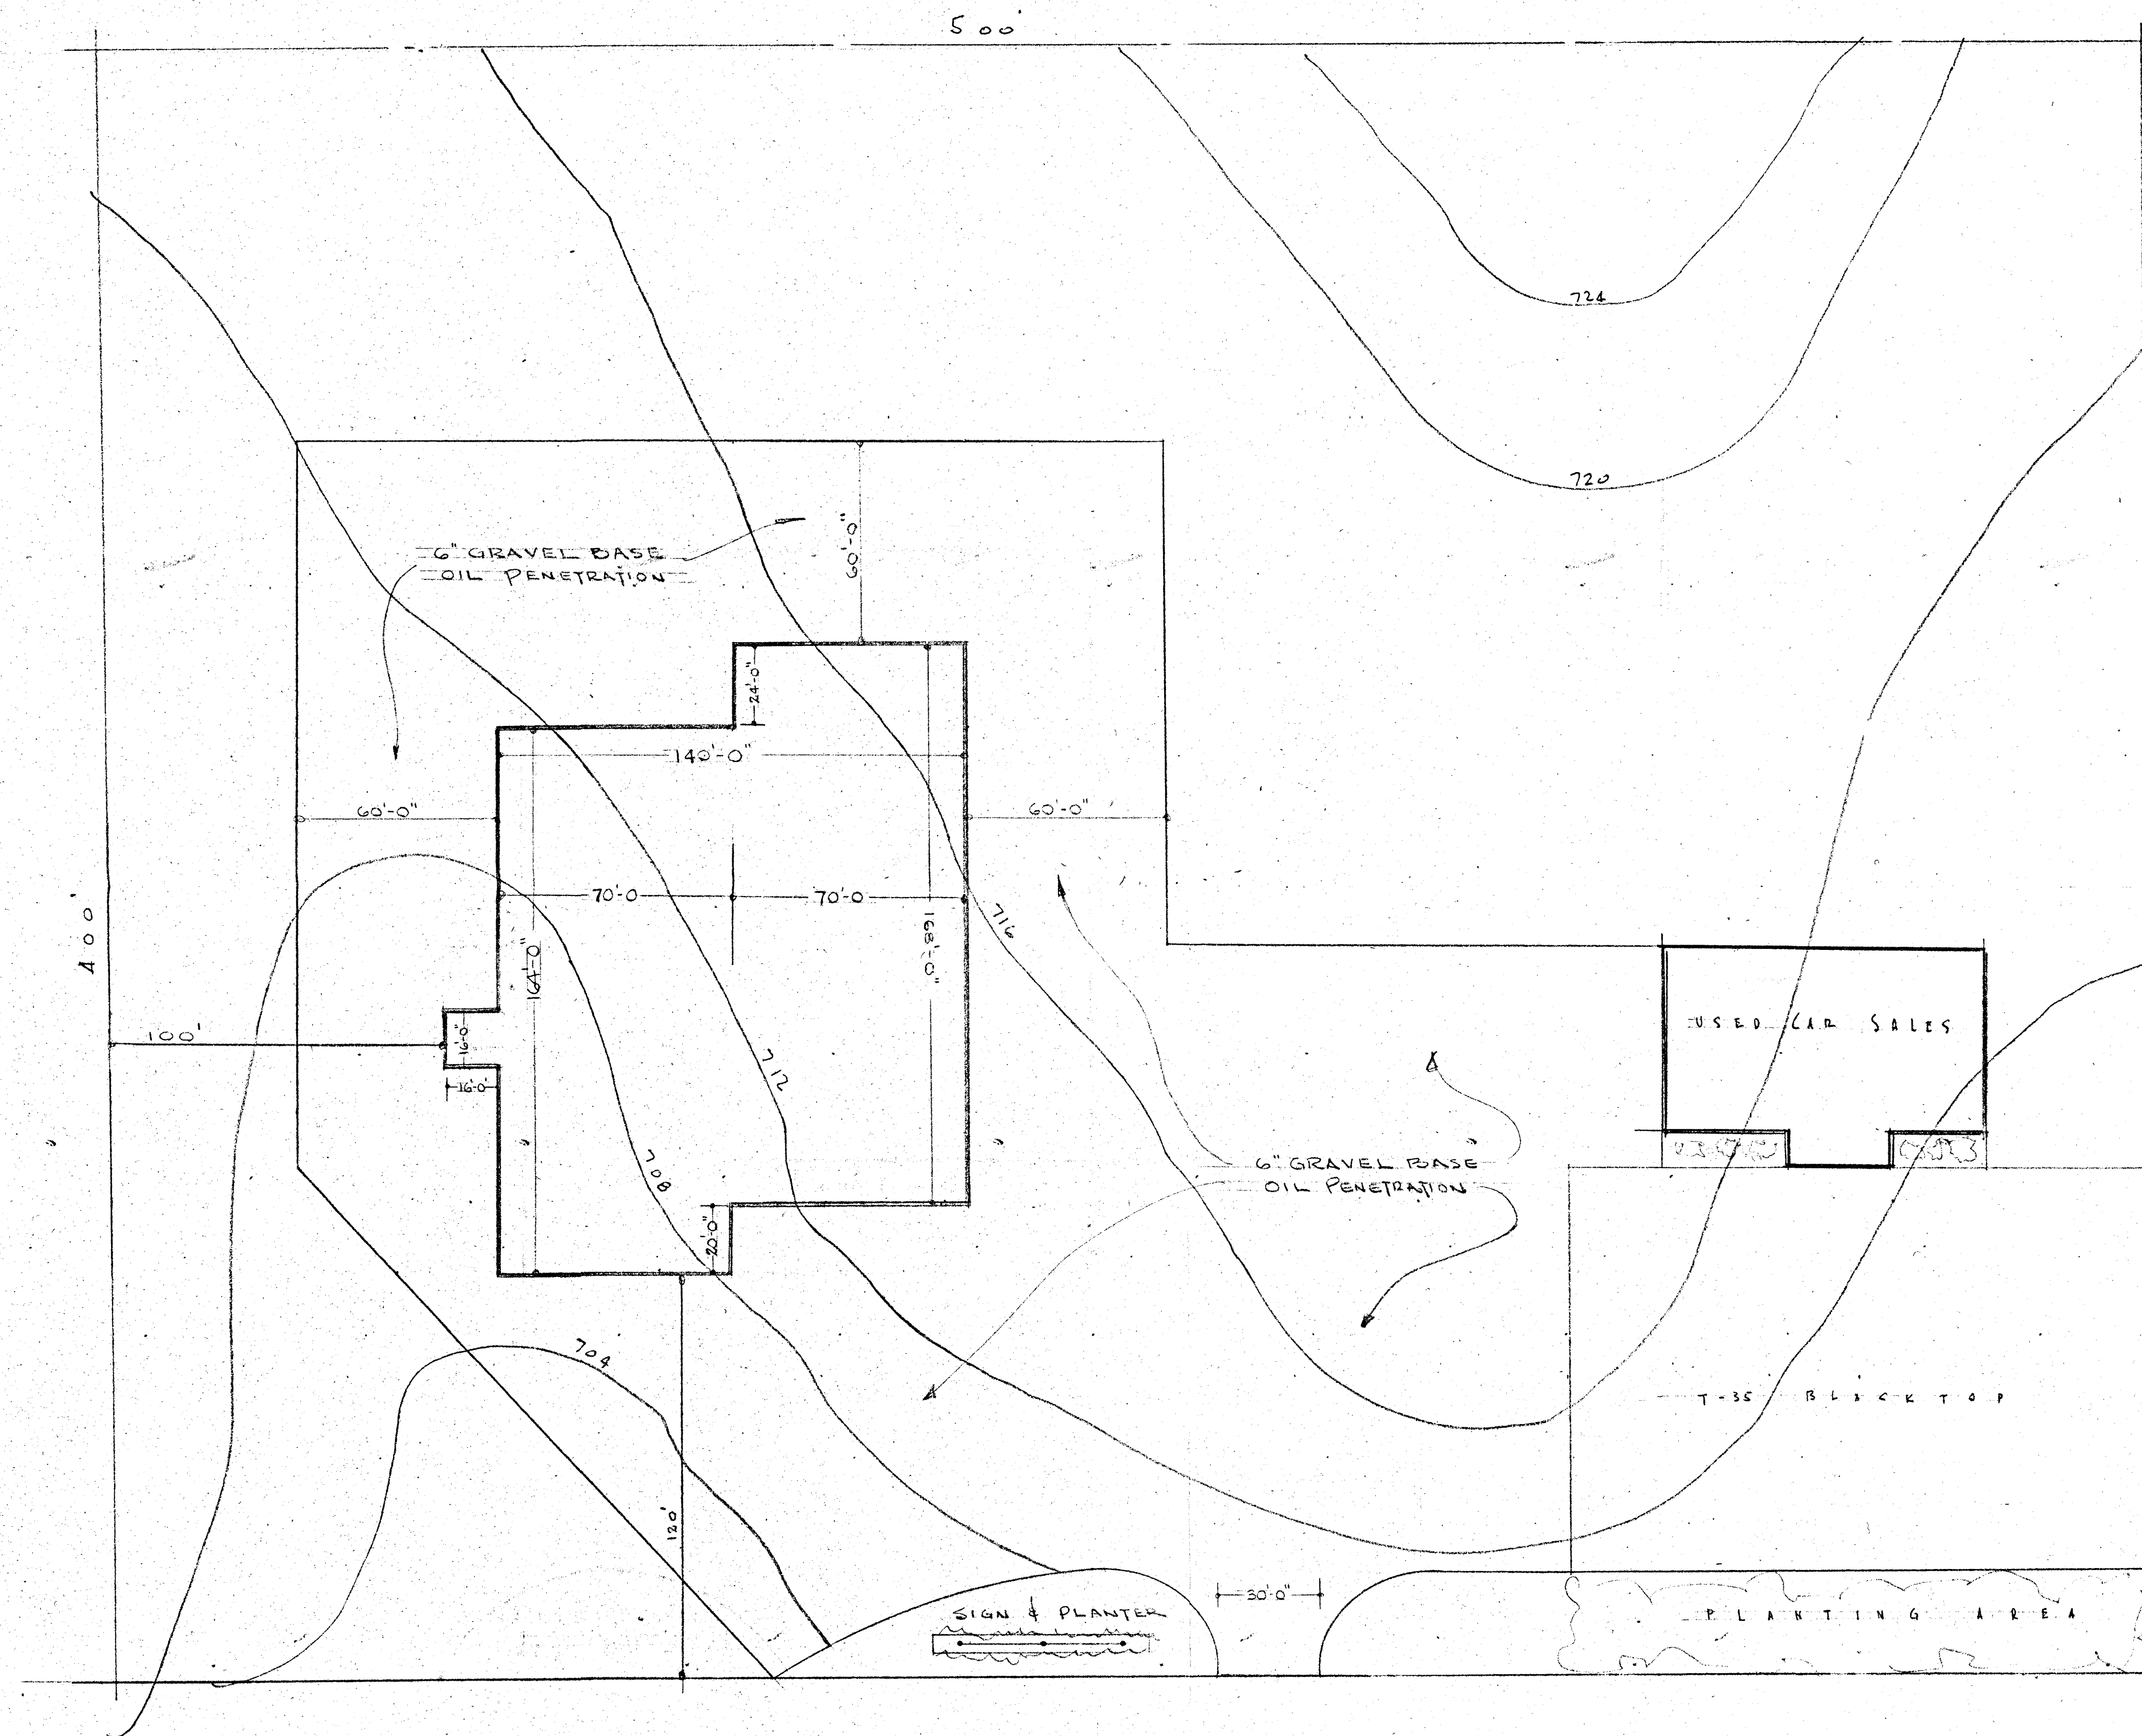





PRELIMINARY PLOT PLAN
SCALE 1" = 30'-0"

HOWARDS CHEVROLET
BLOOMINGTON, IND.
PACKAGED BLDGS. INC.
DAYTON, OHIO

202
12
17

120
140
160
300

100 SOUTH-NORTH FENCE LINE
240 SOUTH-NORTH FENCE LINE
300 NORTH OF R/W LINE OF S.R. #37

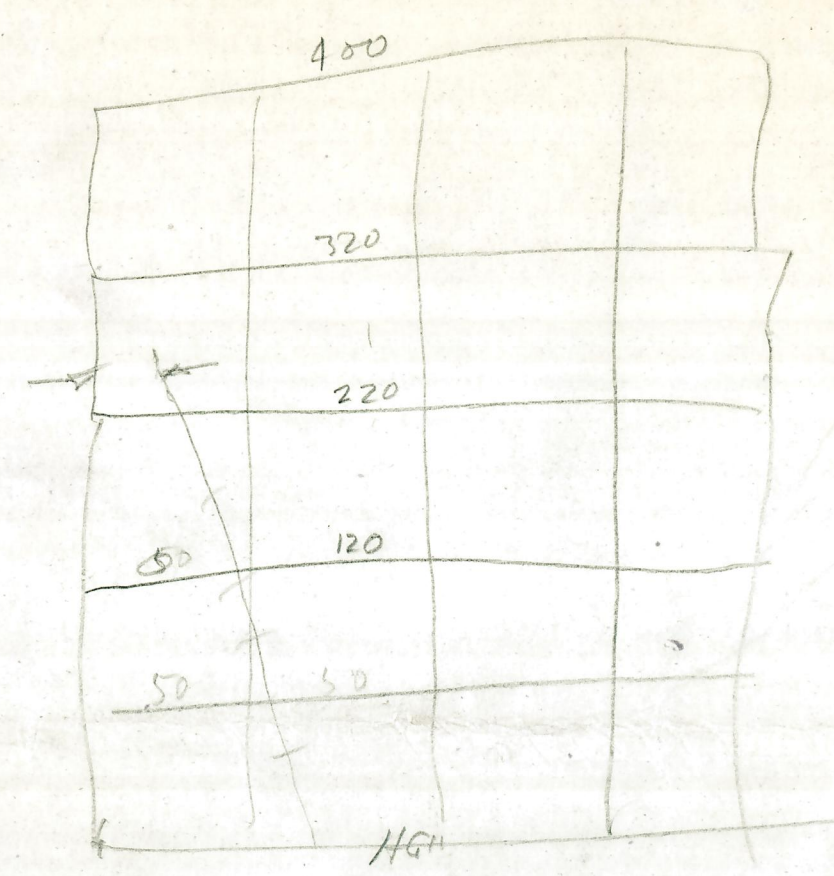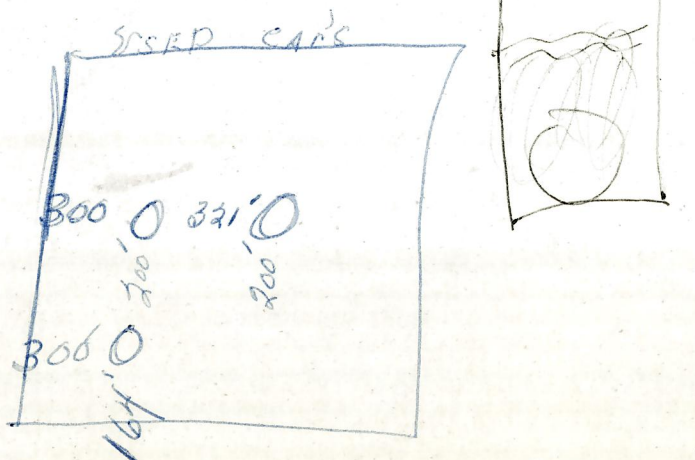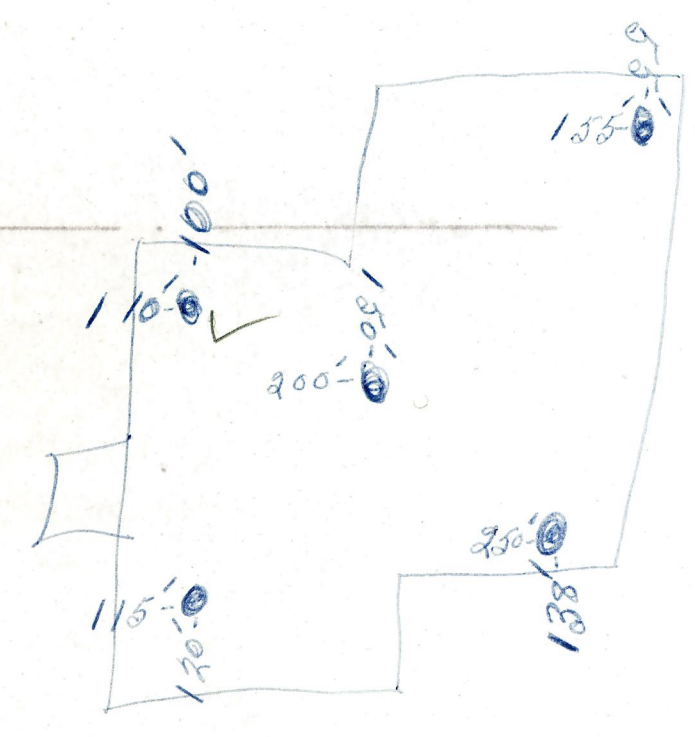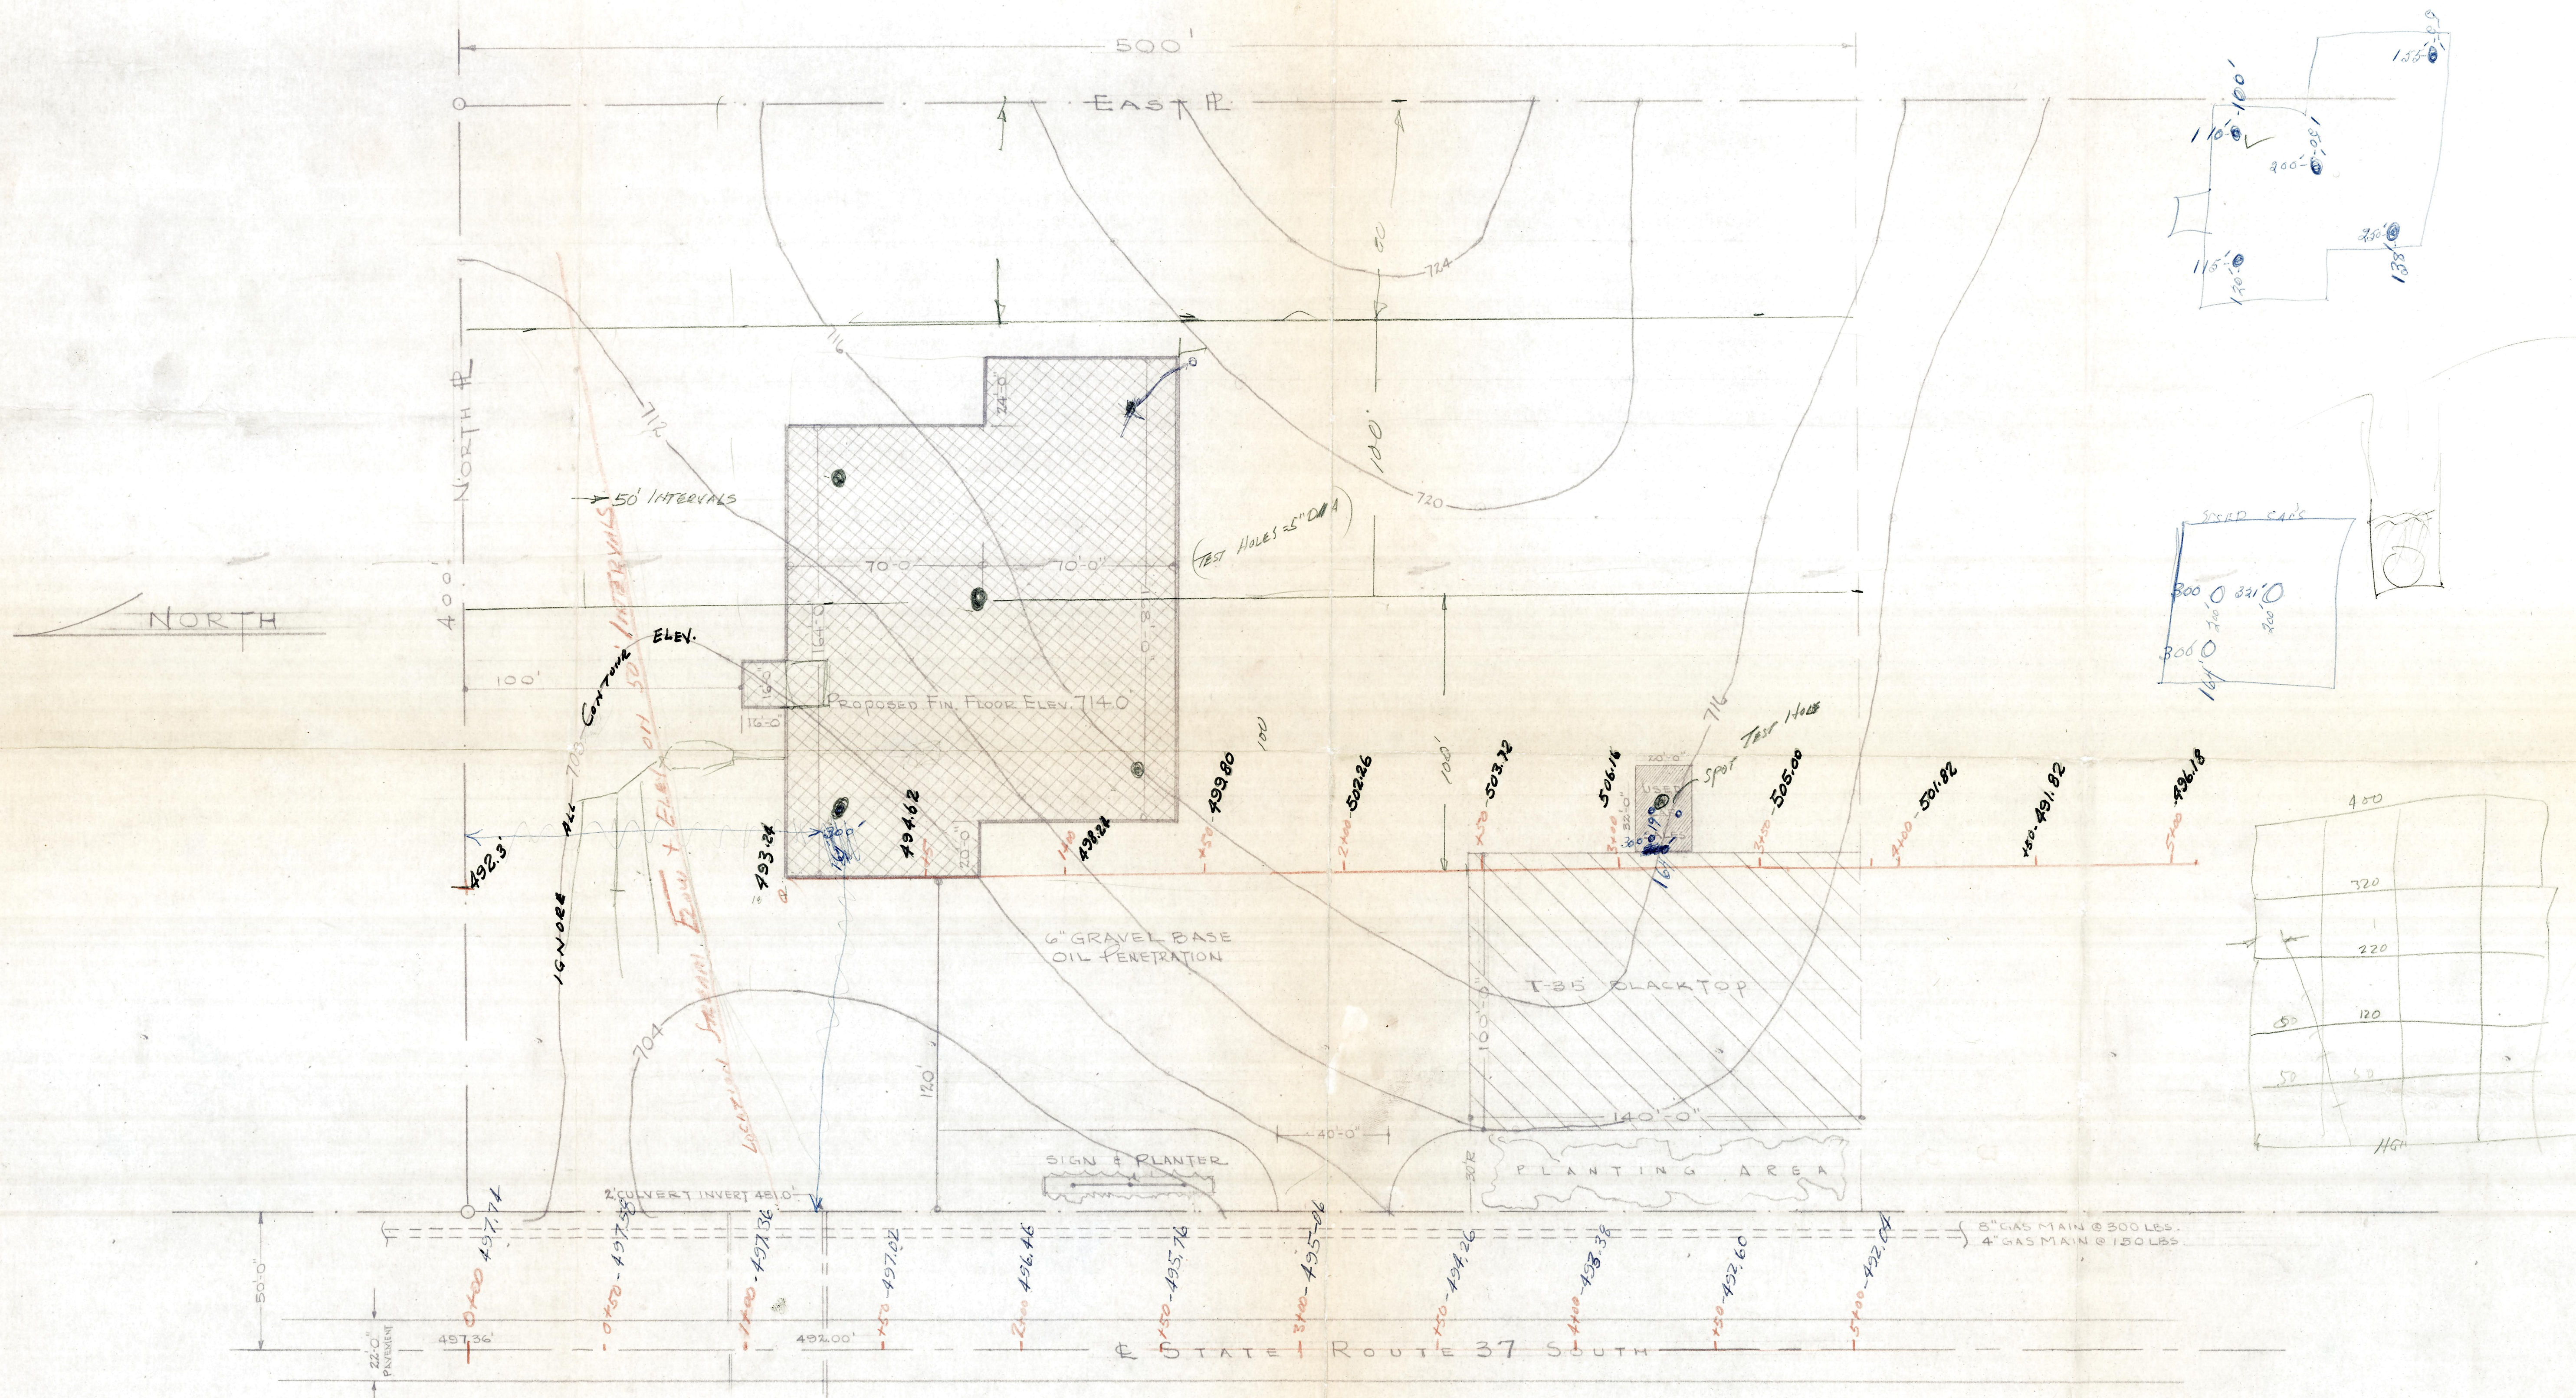

* B.M. Top Fill Hvd. Assumed Elev. of 500.00

CITY OUTFALL SEWER
APPROX. 452' FROM R.
APPROX. 33' PIPE
INVERT M.H. = 478.25'

PRELIMINARY PLOT PLAN
SCALE 1" = 30'-0"

FINDLAY ST
445-NORTH FINDLAY
DAYTON, OHIO

		PACKAGED BUILDINGS, INC.	
DAYTON 253-8994		CINCINNATI 731-8227	
PROJECT No. HOWARD CHEVROLET BLOOMINGTON, IND.			
DRAWN BY	EL	DATE	6.11.62
CHECKED BY		DATE	
REVISIONS		DATE	
APPROVED BY			DATE
CONTRACT NO.			
SHEET			OF
